


Activity ID	Activity Description	Case 1:05-cv-00858-JF	Rem Dur	%	Early Start	Early Finish	Document 127-10 Filed 02/29/2008 Page 1 of 2												
							JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN


### Building A - Administration

1-10-116	DWV & Domestic Piping Rough In	1	90	01JUL03A	31AUG04
1-10-117	HVAC Piping Rough In	0	100	26AUG03A	
1-10-114	Install Ductwork & VAVs	0	100	03SEP03A	30JUN04A
1-10-118	Test Ductwork & Piping	1	80	20FEB04A	31AUG04
1-10-119	Ductwork Insulation	1	90	20FEB04A	31AUG04
12-31-129	Install GRDs	0	100	12JUL04A	16AUG04A

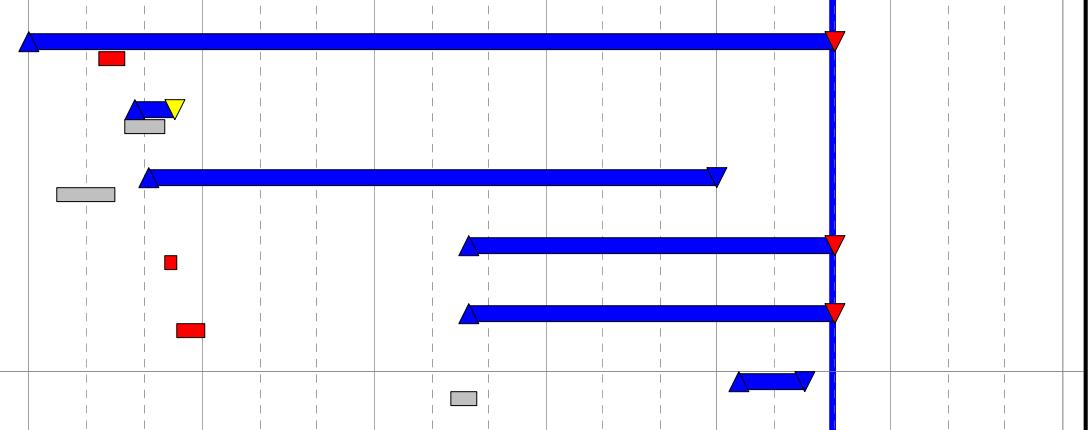


### Building C - Classrooms

2-7-178	DWV/Domestic/Gas Piping Rough In	0	100	01JUL03A	31DEC03A
2-7-180	HVAC Piping Rough In	0	100	01JUL03A	31DEC03A
2-7-176	Install Ductwork & VAVs (VAV 9/30/03)	0	100	15JUL03A	17MAY04A
2-7-181	Test Ductwork & Piping	0	100	23DEC03A	17MAY04A
2-7-182	Ductwork Insulation	0	100	31DEC03A	17MAY04A
12-31-208	Setting Plumbing Fixtures	0	100	03FEB04A	14JUN04A
12-31-209	Install GRDs	0	100	02MAR04A	16MAR04A

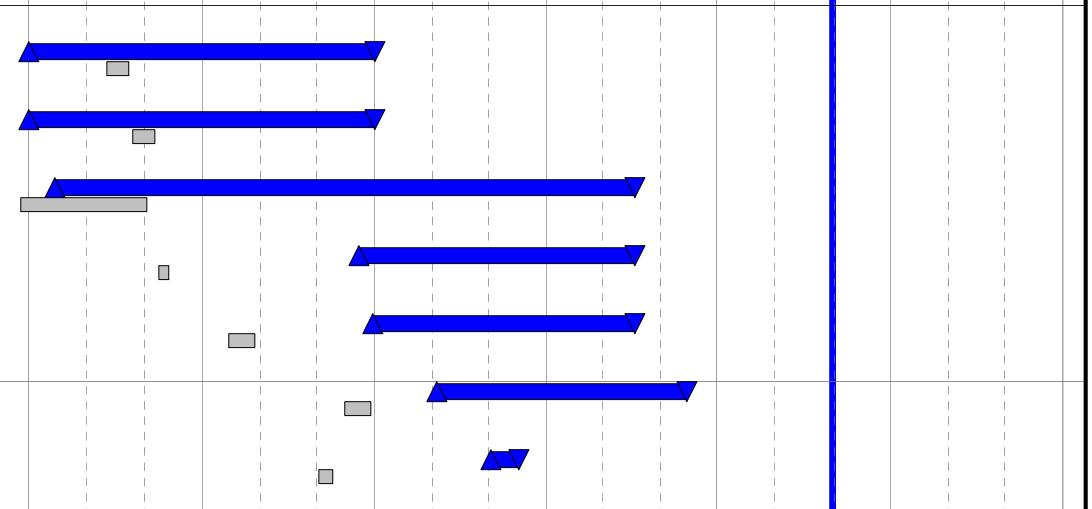

### Building D - Classrooms

2-7-239	DWV/Domestic/Gas Rough In	0	100	14AUG03A	17MAY04A
2-7-240	HVAC Piping Rough In	0	100	14AUG03A	17MAY04A
2-7-237	Install Ductwork & VAVs (9/30 VAV Starts)	0	100	09OCT03A	03FEB04A
2-7-242	Ductwork Insulation	0	100	26NOV03A	03FEB04A
2-7-241	Test Ductwork & Piping	0	100	06JAN04A	17MAY04A

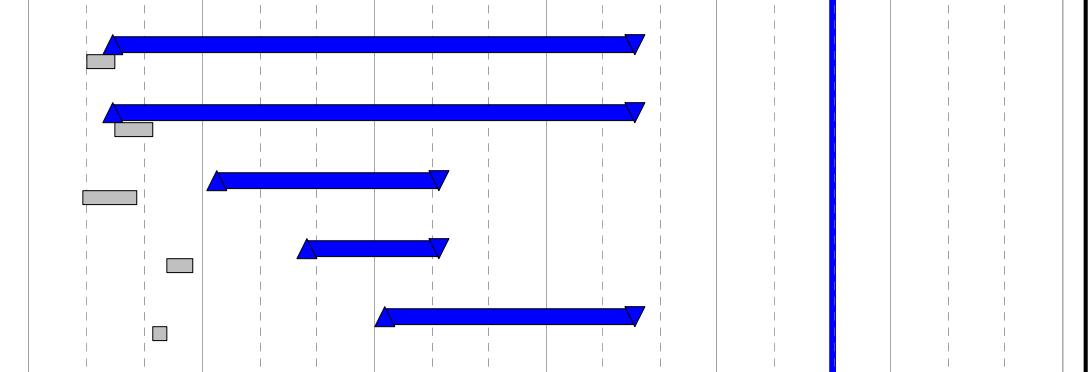

Start Date	18NOV02	RL21	Sheet 1 of 2	Date	Revision	Checked	Approved
Finish Date	10JAN05						
Data Date	31AUG04						
		Early Bar					
		Target Bar					
		Progress Bar					
		Critical Activity					
© Primavera Systems, Inc.		Mechanical Activities 6.31.2003 Target vs. 8.31.2004 Update					

